

PROJECT STATUS

GREECE GARDENS BY SREEDHANYA



31.12.2025

PLOT 1 - APOLLO

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
A	STRUCTURAL & CIVIL WORK		
1	RCC FOR TERRACE FLOOR SLAB	100% COMPLETED	100% COMPLETED
2	RCC FOR RETAINING WALL	100% COMPLETED	100% COMPLETED
B	MASONRY & PLASTERING		
1	BLOCK WORK	12/12 APTS COMPLETED	12/12 APTS COMPLETED
2	CEILING PLASTERING	12/12 APTS COMPLETED	12/12 APTS COMPLETED
3	INSIDE WALL PLASTERING	7/12 APTS COMPLETED	11/12 APTS COMPLETED
4	EXTERNAL PLASTERING	-	30% COMPLETED
C	ELECTRICAL WORK		
1	ELECTRICAL WALL CHASING & BOX FIXING	9/12 APTS COMPLETED	12/12 APTS COMPLETED

PLOT 1 - APOLLO



FRONT ELEVATION WORK IN PROGRESS

PLOT 1 - APOLLO: COMMON AREA WORK IN PROGRESS (1 / 2)



TERRACE CEILING PLASTERING & FLOOR



EXTERNAL
PLASTERING


PLOT 1 - APOLLO: COMMON AREA WORK IN PROGRESS (2/2)



PASSAGE



DUCT

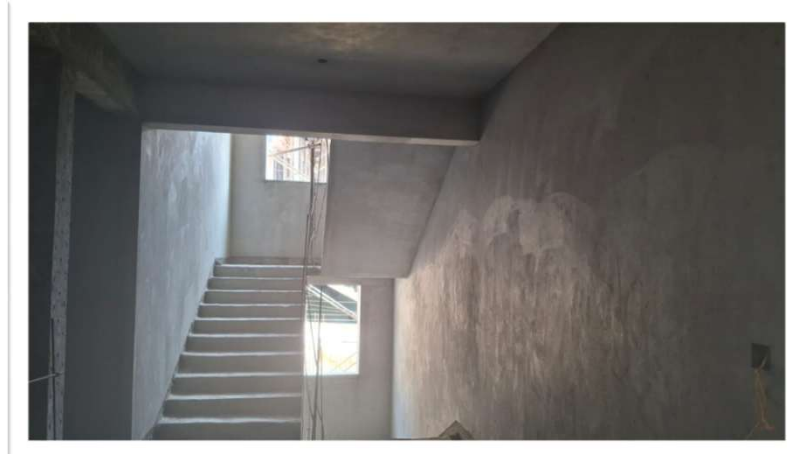

COMMON AREA STAIR

PLOT 1 - APOLLO: APARTMENT INSIDE WORK IN PROGRESS



APT BLOCKWORK & PLASTERING



WATER PROOFING



ELECTRICAL WALL CHASING & BOX FIXING



APT CEILING PLASTERING

PLOT 2 - ATHENS

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
A	STRUCTURAL & CIVIL WORK		
1	RCC FOR COLUMN FOOTING	33/63 COMPLETED	33/63 COMPLETED
2	RCC FOR BF TO GF COLUMN	33/63 COMPLETED	33/63 COMPLETED
3	RCC FOR GF TO FF COLUMN	30/34 COMPLETED	30/34 COMPLETED
4	RCC FOR GF SLAB	60% COMPLETED	60% COMPLETED
5	RCC FOR FF SLAB	30% COMPLETED	40% COMPLETED
6	RCC FOR FF-SF COLUMN	-	23/26 COMPLETED
7	RCC FOR RETAINING WALL	60% COMPLETED	60% COMPLETED

PLOT 2 - ATHENS



ELEVATION VIEWS - WORK IN PROGRESS

PLOT 2 - ATHENS



FLOOR 1 SHUTTERING WORK IN PROGRESS

PLOT 3 - HERMES

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
A	EARTHWORK & EXCAVATION		
1	GENERAL EARTH WORK	COMPLETED	COMPLETED
2	FOUNDATION-EARTH WORK EXCAVATION	40% COMPLETED	75% COMPLETED
B	STRUCTURAL & CIVIL WORK		
1	RCC FOR COLUMN FOOTING	18/51 COMPLETED	30/51 COMPLETED
2	RCC FOR RETAINING WALL	30% COMPLETED	50% COMPLETED

PLOT 3 - HERMES



WORK IN PROGRESS

PLOT 9 - LAMIA

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
1	GENERAL EARTH WORK EXCAVATION	STARTED	ONGOING

PLOT 10 - RHODES

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
A	STRUCTURAL & CIVIL WORK		
1	RCC FOR COLUMN FOOTING	37/47 COMPLETED	43/47 COMPLETED
2	RCC FOR RETAINING WALL	75% COMPLETED	75% COMPLETED
3	RCC FOR BF-GF COLUMN	-	27/51 COLUMN

PLOT 10 - RHODES



COLUMN FOOTING & RETAINING WALL

PLOT 11 - ZEUS

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
A	STRUCTURAL & CIVIL WORK		
1	RCC FOR SHORT COLUMN FOOTING-GROUND FLOOR	28/28 COMPLETED	28/28 COMPLETED
2	RCC FOR RETAINING WALL	60% COMPLETED	60% COMPLETED
3	RCC FOR COLUMN - GROUND FLOOR	31/31 COMPLETED	31/31 COMPLETED
4	RCC BASEMENT FLOOR - GROUND FLOOR COLUMN	-	13/31 COMPLETED
5	RCC FOR GROUND FLOOR SLAB	-	100% COMPLETED
6	GROUND FLOOR-FIRST FLOOR COLUMN	-	10/31 COMPLETED

PLOT 11 - ZEUS



COLUMN FOOTING

BASKET BALL COURT & ELECTRICAL ROOM

SL NO	ITEM OF WORK	SEPTEMBER	DECEMBER
1	STRUCTURAL WORK	100% COMPLETED	100% COMPLETED
2	MASONARY WORK	100% COMPLETED	100% COMPLETED

GREECE GARDENS: EQUIPMENTS IN USE



CONCRETE MIXER



PUTZ MAISTER

THANK YOU
